1520 W. Cameron Ave., Suite 103 ◆ West Covina, CA 91790
Ph. 626-962-4436 ◆ Fx. 626-962-4437 ◆ www.globalenvirotraining.com

Asbestos / Close-Out / Report

Job Site:

CALIFORNIA STATE UNIVERSITY LOS ANGELES (CSULA)
KING HALL
FLOOR 4 – ROOM C4030
5151 STATE UNIVERSITY DR.
LOS ANGELES, CA 90032

Prepared For:

MS. BARBARA QUEEN
CALIFORNIA STATE UNIVERSITY LOS ANGELES (CSULA)
5151 STATE UNIVERSITY DR.
LOS ANGELES, CA 90032

PROJECT №. **E224-316**

December 3, 2024

Mario Virgen
State of California
Certified Asbestos Consultant #00-2859

Copyright © 2024 Global Environmental Training & Consulting, Inc. All Rights Reserved

TABLE OF CONTENTS

- EXECUTIVE SUMMARY _____ 1.0
- DAILY FIELD LOGS _____ 2.0
- DAILY AIR LOGS _____ 3.0
- ASBESTOS AIR LAB RESULTS _____ 4.0
- CLEARANCE CERTIFICATIONS _____ 5.0
- NOTIFICATIONS _____ 6.0
- INSPECTOR'S CERTIFICATION _____ 7.0
- CONTRACTOR PERSONNEL _____ 8.0
- WORKER'S SUBMITTALS _____ 9.0
- SCHEMATIC _____ 10.0

Copyright © 2024

All Rights Reserved

1.0 EXECUTIVE SUMMARY

Copyright © 2024

All Rights Reserved

EXECUTIVE SUMMARY

Global Environmental Training & Consulting, Inc. (GETC) was retained at the request of California State University Los Angeles (CSULA). GETC was contracted to perform Project Management and Asbestos Clean-Up Monitoring for CSULA – King Hall – 4th Floor – Room C4030 located at 5151 State University Dr., in Los Angeles, California.

The sequence for this project was November 21, 2024, through November 22, 2024. GETC monitored the Asbestos Clean-Up of Room C4030 on the 4th Floor within King Hall throughout the course of this project. GETC's onsite inspector ensured the contractor's compliance with all local, state and federal regulations current as of November 21, 2024. This included but was not limited to the contractor's work area preparation, engineering controls, and worker protection and work practices. The contractor implemented HEPA Vacuuming and Wet Wiping methods and engineering controls on this project to control potential contamination of areas adjacent to the containment.

The contractor was responsible for monitoring his workers for potential exposure during normal work activities.

Copyright © 2024 Global Environmental Training & Consulting, Inc. All Rights Reserved

2.0 DAILY FIELD LOGS

Copyright © 2024

All Rights Reserved

Global Environmental Training & Consulting, Inc.

DAILY OBSERVATION LOG

Project Name: **KING HALL – 4TH FLOOR – ROOM C4030**	Date: 11/21/24
GETC Project No. **E224-316**	Contractor: Tri Span
Address: **5151 STATE UNIVERSITY DR. LOS ANGELES, CA 90032**	Contractor's Supervisor: Alejandro Espinoza
Page: 1 of 1	Crew Size: Sup + 1

(Print all Entries in Blue or Black Ink, Use Military Time ONLY)

1400 – Getc rep on site along with Tri Span crew. Scope of work for this project is to decontaminate (hepa vacuum and wet wipe) in Room C4030.

1430 – Barbara from CSULA on site to open door at King Hall, Room C4030.

1500 – TriSpan crew has mobilized equipment to work area. They will now set up critical barrier on door then install 3-stage decon. Inside room, they will cover critical barriers with poly then start clean up.

1630 – Tri Span crew has completed set up and they will now suit up in PPE and start removal.

1800 – Crew breaks for lunch.

1900 – Crew returns from lunch. They will suit up in PPE and start wet wiping.

2100 – TriSpan crew continues wet wiping in Room C4030. No problems to report.

2230 – Crew has completed cleanup. Getc rep off site.

Description of Material to be ~~Abated~~: Clean-up	Location of Material to be Abated: C4030
Quantity of Material to be Abated (SF/LF):	CSST/CAC/CDPH No. 18-6224
Inspector's Name (print): Sergio Perez	Inspector's Signature:

Global Environmental Training & Consulting, Inc.

DAILY OBSERVATION LOG

Project Name: **KING HALL – 4TH FLOOR – ROOM C4030**	Date: 11/22/24
GETC Project No. **E224-316**	Contractor: Tri Span
Address: **5151 STATE UNIVERSITY DR. LOS ANGELES, CA 90032**	Contractor's Supervisor: Alejandro Espinosa
Page: | of |	Crew Size: Sup

(Print all Entries in Blue or Black Ink, Use Military Time ONLY)

1100 – Getc rep on site along with TriSpan Sup. Scope of work for today is to perform TEM air clearances.

1115 – TEM Air clearances have been set in Room C4030.

1325 – TEM Air clearances have been pulled.

1335 – Getc rep off site.

Description of Material to be Abated: TEM Clearances	Location of Material to be Abated: C4030
Quantity of Material to be Abated (SF/LF):	CSST/CAC/CDPH No. 18-6224
Inspector's Name (print): Sergio Perez	Inspector's Signature:

1520 W. CAMERON AVE., SUITE 103 ◆ WEST COVINA, CA 91790
OFFICE: 626.962.4436 ◆ FAX: 626.962.4437
www.globalenvirotraining.com

3.0 DAILY AIR LOGS

Copyright © 2024

All Rights Reserved

Global Environmental Training & Consulting, Inc.

Client:	Project Name/Location:	GETC Project No. **E224-316**
CSULA – MIKE MORALES **5151 STATE UNIVERSITY DR.** **LOS ANGELES, CA 90032**	**KING HALL – 4TH FLOOR** **ROOM C4030** **5151 STATE UNIVERSITY DR.** **LOS ANGELES, CA 90032**	Sample Collection By: Sergio Perez Sample Analysis By: Sergio Perez Page 1 of 1

Date:	Means of Pump Calibration:	Microscope Field Area	PCM Filter	TEM Filter	Cassette Manufacturer: EMS
11/21/24	☐ Gilibrator ☒ Calibrated Rotometer	☒ 0.00785 sq mm ☐ sq mm	☒ 0.8um 25 mm ☐ 0.8um 37 mm	☐ <0.45um 25 mm ☐ <0.45um 37mm	Lot # 20230302

Sample#	Type	Sample Description Location	Time (24 Hour Clock) Activity	Start	Stop	Total minutes	Flow Rate (L/Min) Start	Stop	Total Flow Avg.	Air Volume (Liters)	Fibers/Fields Minus Avg. Blank	RESULTS f/cc s/mm
A-01	PCM	Field Blank										
A-02	L	Hallway	DCON	1500	2200	420	4	4	4	1,680	7/100	0.00204333

ACTIVITY CODES INSIDE WORK AREA			ACTIVITY CODES OUTSIDE WORK AREA	
↑PRE=BACKGROUND	↑IWA=INSIDE WORK AREA,		↑EXH=EXHAUST	↑DCON=DECON
↑PER=PERSONAL SURVEY	↑ CLR=CLEARANCE	↑AS=AIR	↑CB=CRITICAL BARRIER ↑GB=GLOVEBAG	↑OSWA=OUTSIDE WORK AREA

DAILY AIR LOG

OFFICE: 626.962.4436 ◈FAX: 626.962.4437
1520 W. CAMERON AVE., SUITE 103◈WEST COVINA, CA 91790◈www.globalenvirotraining.com

4.0 ASBESTOS AIR LAB RESULTS

All Rights Reserved

AMERI SCI
www.amerisci.com

Asbestos / Lead Analysis Chain of Custody

AMERISCI JOB #: 124111784

AMERISCI LOS ANGELES
24416 S Main St. Suite 308
Carson, CA 90745
Phone (310) 834-4868
Fax (310) 834-4772

COMPANY:	ADDRESS:	P.O.#:
GLOBAL ENVIRONMENTAL TRAINING & CONSULTING, INC.	1520 W. CAMERON AVE. #103 WEST COVINA, CA 91790	

PROJECT INFORMATION	ANALYSIS TYPE	TURNAROUND TIME						AIR FILTER INFORMATION:	
		RUSH	24 HR	48 HR	72 HR	5 DAY	OTHER		
JOB NAME: KING HALL - 4TH FL. - RM. C4030	TEM AHERA		X					MCE	X
	PLM Bulk							PC	
JOB NUMBER: E224-316	PCM Air							25 mm	
	PLM 1000 P.C.							37 mm	X
JOB MANAGER:	Lead Air							0.45 um	
	Lead Wipe							0.80 um	X
JOB DESCRIPTION:	Lead Paint / Soil							TEMP:	
	OTHER:							OTHER:	

INITIAL RESULTS DELIVERY: ☐ FAX ☒ EMAIL ☐ VERBAL ☐ MAIL ONLY
RETURN SAMPLES YES ☐
REPORTS TO: STAFF@GLOBALENVIROTRAINING.COM / MARIO.VIRGEN@GLOBALENVIROTRAINING.COM MIGUEL.VIRGEN@GLOBALENVIROTRAINING.COM
PHONE:
INVOICE TO: ACCOUNTING@GLOBALENVIROTRAINING.COM
FAX:
COMMENTS: Do not analyze blanks
EMAIL:
CELL:

SAMPLE ID	SAMPLE LOCATION	START TIME	STOP TIME	TOTAL TIME	X LITERS /MIN.	= TOTAL VOLUME	DATE COLLECTED
T-01	Room C4030	1115	1325	130	9.9	1,287	11/22/24
T-02	Room C4030	1115	1325	130	9.9	1,287	1
T-03	Field Blank Inside						
T-04	Field Blank Outside						
T-05	Sealed Blank						

SAMPLED BY:	DATE/TIME:	RECEIVED BY:	DATE/TIME:
Sergio Perez	11/22/24 1115		
RELINQUISHED BY:	**DATE/TIME:**	**RECEIVED BY:**	**DATE/TIME:**
[signature]	11/23/24 1025	[signature]	11/25/24 @ 0800
RELINQUISHED BY:	**DATE/TIME:**	**RECEIVED IN LAB BY:**	**DATE/TIME:**
[signature]	11/25/24 @ 900	[signature]	11/26/24

AmeriSci Richmond
13635 GENITO ROAD
MIDLOTHIAN, VIRGINIA 23112
TEL: (804) 763-1200 • FAX: (804) 763-1800

November 26, 2024

Global Environmental Training
Attn: Mario Virgen
1520 W. Cameron Ave.
Suite 103
West Covina, CA 91790

RE: Global Environmental Training
Job Number 124111784
P.O. #E224-316
E224-316; King Hall - 4th Fl - RM C4030

Dear Mario Virgen:

Enclosed are the results for TEM fiber analysis of the following Global Environmental Training samples received at AmeriSci on Tuesday, November 26, 2024, for a 6-8 hour turnaround:

T-01, T-02, T-03, T-04, T-05

The 5 air samples were sent to AmeriSci via Fed Ex 7178 3973 8466 B. These samples were prepared according to AHERA Protocol. AHERA Clearance requirements for sampling, including required blanks are mandated in 40 CFR 763, Subpart E, Appendix A, available at www.epa.gov/asbestos/pubs/asbreg.html.

Table I represents a summary of all pertinent information used for the structure (fiber) density and concentration calculations. Included are the size of each structure counted, the structure density and concentration, type of fibrous material detected and the analytical sensitivity, which represents the concentration by the detection of one structure in the TEM structure count. Copies of the Fiber Count Sheets are included. These data sheets contain information for structure length/width, structure type, structure morphology and pertinent information on EDS, SAED and photography.

This report relates ONLY to the sample analysis expressed as structure density. The CV for this analysis is expected to range from 0.3 to 1.2, depending on the quantity of the analyte present. AmeriSci assumes no responsibility for customer supplied data such as "sample location" or "air volume sampled". This report must not be used to claim product endorsement by AmeriSci, NVLAP or any agency of the U. S. Government. The National Institute of Standards and Technology accreditation requirements, mandate that this report must not be reproduced, except in full without the written approval of the laboratory.

AmeriSci appreciates this opportunity to serve your organization. Please contact us for any further assistance or with any questions.

Sincerely,

Cory M. Parnell

Laboratory Director | Authorized Signatory

AmeriSci Job #: **124111784**

Client Name: Global Environmental Training

Table I
Summary of Transmission Electron Microscopy (TEM) Results for Asbestos in Air by 40 CFR 763 APX A No III

E224-316; King Hall - 4th Fl - RM C4030

AmeriSci Sample #	Client Sample #	Dilution Factor	Air Filtered (liters)	Area Analyzed (sq. mm.)	* Analytical Sensitivity (struc/cc air)	Asbestos Structures Detected (Microns)			Structure Density (struc/sq mm)		Structure Concentration (struc/cc air)		Type of Asbestos
						0.5-5.0	>=5.0	Total	>=5.0	Total	>=5.0	Total	
01 inside	T-01		1287	.060	0.0050	0.0	0.0	0.0	<16.6	<16.6	<0.0050	<0.0050	NSD
Location: Room C4030													
02 inside	T-02		1287	.060	0.0050	0.0	0.0	0.0	<16.6	<16.6	<0.0050	<0.0050	NSD
Location: Room C4030													
03 blank**	T-03		0										
Location: Field Blank Inside													
04 blank**	T-04		0										
Location: Field Blank Outside													
05 blank**	T-05		0										
Location: Sealed Blank													

Reviewed By: Cory M. Parnell

Analyzed By: Cory M. Parnell


Date: 11/26/2024

NVLAP#: 101904-0

* concentration represented by the detection of 1 structure ** not analyzed NSD: No Asbestos Structures Detected

Note: Customer supplied information in this report can affect validity of results. Reported values of Struct/cc air are not covered by NVLAP accreditation.

TEM Asbestos (air) Count Sheet



Client Name: Global Environmental Training
Job #: 124111784
Lab Sample #: 01
Client Sample #: T-01
Received: 11/26/24 12:00:00
Date Analyzed: 11/26/24

Volume (liters): 1 287.0
Filter Type / Filter Area: MCE 385 mm2
Grid Opening Size: 0.01003 mm2
Area Examined: 0.06018 mm2
Magnification: 20,000
Accelerating Voltage: 100 KeV

Analysis Performed by: Cory M. Parnell

Location	Grid Opening	Fiber	Length µm	Width µm	Fiber Type	Morphology	EDS	Orient.	SAED	Photo
C7-B5/1	1	NSD							☐	
C7-C5/1	2	NSD							☐	
C7-E5/1	3	NSD							☐	
C6-C3/4	4	NSD							☐	
C6-E3/4	5	NSD							☐	
C6-F3/4	6	NSD							☐	

NSD: No Asbestos Structures Detected

Analysis Method: 40 CFR 763 APX A No III
Scope #: Front 4: Jeol JEM-100CX II, Serial No.156147-247


Comments

		Structure Density (str/mm2)	UCL (str/mm2)	Concentration (str/cc air)
Total Grids Analyzed:	2			
Total Grid Openings:	6			
Chrysotile Asbestos Structures:	0	<16.6	<18.2	<0.0050
Amphibole Asbestos Structures:	0	<16.6	<18.2	<0.0050
Asbestos Structures >=5 microns:	0	<16.6	<18.2	<0.0050
Total Non-Asbestos Structures:				
Total Asbestos Structures:	0	<16.6	<18.2	<0.0050
Analytical Sensitivity:		16.6		

Grid Evaluation

- ☑ Grid Openings Covered > 50%
- ☑ Intact Grid Opening > 50%
- ☑ Undissolved Filter < 10%
- ☑ Folded Replica < 50%
- ☑ Filter Loading < 10%
- ☑ Particulate Even

TEM Asbestos (air) Count Sheet



Client Name: Global Environmental Training
Job #: 124111784
Lab Sample #: 02
Client Sample #: T-02
Received: 11/26/24 12:00:00
Date Analyzed: 11/26/24

Volume (liters): 1 287.0
Filter Type / Filter Area: MCE 385 mm2
Grid Opening Size: 0.01003 mm2
Area Examined: 0.06018 mm2
Magnification: 20,000
Accelerating Voltage: 100 KeV

Analysis Performed by: Cory M. Parnell

Location	Grid Opening	Fiber	Length µm	Width µm	Fiber Type	Morphology	EDS	Orient.	SAED	Photo
C9-C4/4	1	NSD							☐	
C9-E4/4	2	NSD							☐	
C9-F4/4	3	NSD							☐	
C10-C5/4	4	NSD							☐	
C10-E5/4	5	NSD							☐	
C10-F5/4	6	NSD							☐	

NSD: No Asbestos Structures Detected

Analysis Method: 40 CFR 763 APX A No III
Scope #: Front 4: Jeol JEM-100CX II, Serial No.156147-247

Comments

		Structure Density (str/mm2)	UCL (str/mm2)	Concentration (str/cc air)
Total Grids Analyzed:	2			
Total Grid Openings:	6			
Chrysotile Asbestos Structures:	0	<16.6	<18.2	<0.0050
Amphibole Asbestos Structures:	0	<16.6	<18.2	<0.0050
Asbestos Structures >=5 microns:	0	<16.6	<18.2	<0.0050
Total Non-Asbestos Structures:				
Total Asbestos Structures:	0	<16.6	<18.2	<0.0050
Analytical Sensitivity:		16.6		

Grid Evaluation
- ☑ Grid Openings Covered > 50%
- ☑ Intact Grid Opening > 50%
- ☑ Undissolved Filter < 10%
- ☑ Folded Replica < 50%
- ☑ Filter Loading < 10%
- ☑ Particulate Even

5.0 CLEARANCE CERTIFICATIONS

Copyright © 2024

All Rights Reserved

Global Environmental Training & Consulting, Inc.

ASBESTOS AIR MONITORING
CLEARANCE CERTIFICATION

CLIENT:	**CSULA – MIKE MORALES**
PROJECT NAME:	**KING HALL – 4TH FLOOR – ROOM C4030**
LOCATION:	**5151 STATE UNIVERSITY DR., LOS ANGELES, CA 90032**
CONTRACTOR:	Tri Span
CONTRACTOR REP:	Alejandro Espinosa
PROJECT#:	**E224-316**
CERTIFICATE#:	1 of 1
GETC REP:	Sergio Perez

Based on visual observations, and project documentation, the Abatement of the (Project or Phase) referenced as (list specific scope of work)

hepa vaccum and wet wipe inside of Room C4030

has been determined to be in compliance to the best of Consultants knowledge, documentation, and belief to be substantial complete and in accordance with all current local, state and federal regulations. As of Date of Issuance of this Certificate, Client and/or Contractor may proceed with replacement Work upon receipt of this Certification. All clearance samples were well below the (PCM/TEM) Clearance criteria of (<0.01 f/cc) (<70 s/mm).

GETC REPRESENTATIVE	TITLE	DATE
[signature]	CSST	11/22/24

The undersigned Contractor certifies to the best of the Contractor's knowledge, information and belief, that Work identified above has been completed in accordance with all current local, state and federal regulations.

CONTRACTOR REPRESENTATIVE	TITLE	DATE
Alejandro Espinosa	Supervisor	1/22/24

WORK AREA(S) PASS	WORK AREA(S) FAIL
X	

1520 W. CAMERON AVE., SUITE 103 ◆ WEST COVINA, CA 91790
OFFICE: 626.962.4436 ◆ FAX: 626.962.4437
www.globalenvirotraining.com

6.0 NOTIFICATIONS

Copyright © 2024

All Rights Reserved

Global Environmental Training & Consulting, Inc.

NOTICE TO CONTRACTOR

CLIENT: **CSULA – MIKE MORALES**	NOTICE TO: Alejandro Espinosa
PROJECT NAME: **KING HALL – 4TH FLOOR – ROOM C4030**	PROJECT MONITOR: Sergio Perez
CONTRACTOR: TriSpan	DATE: 11/22/24 TIME (24 HR):
GETC PROJECT NO. **E224-316**	PAGE: 1 OF 1

The following checked Notice is hereby issued to the Contractor. The Contractor may proceed with the next phase of Work when applicable or shall comply with the requirements of this Notice as stipulated by the Specifications. Failure of the Owner, Owner's Representative or Consultant to notice unacceptable means, methods, work practices, or results during Contractor's work will not absolve the Contractor from his responsibility to complete the Work in accordance with all current applicable local, state and federal regulations. (Note: Monitor check only one Notice)

- [X] SUCCESSFUL PRE-ABATEMENT INSPECTION
- [X] SUCCESSFUL INTIAL REVIEW
- [X] SUCCESSFUL FINAL VISUAL CLEARANCE INSPECTION
- [X] SUCCESSFUL CLEARANCE TEST
- [ ] STOP WORK (See Note Below)
- [ ] RESUME WORK
- [ ] OTHER (See Comments Below)

Notice to Contractor if Stop Work is issued:
Please be advised that the following work is not in compliance with contract documents. Unless stipulated otherwise by this Notice, the Contractor shall not continue or resume Work until all non-compliance issues are corrected to the satisfaction of the Owner/Consultant and a written Notice to Resume Work is issued to the Contractor.

LOCATION(S) Room C4030

COMMENTS (Identify referenced document, section, article, job log, etc. if applicable)

MONITOR'S SIGNATURE	CONTRACTOR'S REP. SIGNATURE
CSSI	Supervisor
TITLE	TITLE

Signature of the Contractor's Representative is acknowledged of receipt of this Notice and is not admission of non-compliance Contract Documents.

1520 W. CAMERON AVE., SUITE 103 ◆ WEST COVINA, CA 91790
OFFICE: 626.962.4436 ◆ FAX: 626.962.4437
www.globalenvirotraining.com

7.0 INSPECTOR'S CERTIFICATION

Copyright © 2024

All Rights Reserved

State of California
Division of Occupational Safety and Health
Certified Site Surveillance Technician



Sergio R Perez-Loa
Name

Certification No. **18-6224**

Expires on **05/15/25**

This certification was issued by the Division of Occupational Safety and Health as authorized by Sections 7180 et seq. of the Business and Professions Code.

State of California
Division of Occupational Safety and Health
Certified Asbestos Consultant



Mario A Virgen
Name

Certification No. **00-2859**

Expires on **01/05/25**

This certification was issued by the Division of Occupational Safety and Health as authorized by Sections 7180 et seq. of the Business and Professions Code.

8.0 CONTRACTOR PERSONNEL

Copyright © 2024 Global Environmental Training & Consulting, Inc. All Rig

Global Environmental Training & Consulting, Inc.

CONTRACTOR PERSONNEL

Client:	Project Name/Location:
CSULA – MIKE MORALES **5151 STATE UNIVERSITY DR.** **LOS ANGELES, CA 90032**	**KING HALL – 4TH FLOOR** **ROOM C4030** **5151 STATE UNIVERSITY DR.** **LOS ANGELES, CA 90032**
GETC PROJECT NO. **E224-316**	AREA: C4030
GETC REP: Sergio Perez	DATE: 11/21/24
CONTRACTOR: TriSpan	PAGE NO. 1 of 2

EMPLOYEE NAME	TRNG EXP.	PHYS EXP.	FIT EXP.	DATES WORKED 11/21	11/22			
*Alejandro Espinosa	6/8/25	12/5/24	12/5/24	✓	✓			
Eloy Sepulveda	10/19/25	11/25/24	11/25/24	✓	—			

NOTE: DATES PROVIDED ARE THE EXPIRATION DATES FOR WORKER'S SUBMITTALS * = SUPERVISOR

1520 W. CAMERON AVE., SUITE 103◈WEST COVINA, CA 91790
OFFICE: 626.962.4436◈FAX: 626.962.4437
www.globalenvirotraining.com

9.0 WORKER'S SUBMITTALS

Copyright © 2024

All Rights Reserved

ECOLOGICS™
TRAINING INSTITUTE

Certificate of Attendance

CERTIFICATE NUMBER
63706

This is to Certify that

ALEJANDRO ESPINOSA

Has Completed the Course of

AHERA ASBESTOS ABATEMENT CONTRACTOR/SUPERVISOR 8 HR. REFRESHER COURSE CA-014-04

UNDER TSCA 206, FOR PURPOSES OF COMPLIANCE WITH 29 CFR 1926.1101 AND TITLE 8 CCR 1529 AND TITLE 8 CCR 5208.

ARMANDO DUCOING
DIRECTOR

June 08, 2024	E060824CSR 060824	June 08, 2025
COMPLETION DATE	CLASS NUMBER / STARTING DATE	CERTIFICATE EXPIRES

Ecologics Training Institute

2487 E Orangethorpe Ave . Fullerton, CA 92831 . Ph (714) 632-8100 . Fax (714) 632-8111 . www.ecologicsonline.com

DOUGLAS INDUSTRIAL MEDICAL CLINIC

PHYSICIAN'S WRITTEN OPINION – ASBESTOS

COMPANY: HARBOR ENVIRONMENTAL

Applicant's Name: ALEJANDRO ESPINOZA

Applicant's Address: 7402 MARBRISA AVE HUNTINGTON PARK, CA 90255

" The above named individual was seen by me on, 12/05/2023 and in accordance with all applicable portions of OSHA's Asbestos Standard for the Construction Industry, 29 CFR 1926.1101, with which I am familiar, I have indicated by initials, that I have performed the following."

1. D.O. Reviewed with this individual, his/her completed OSHA standardized Medical questionnaire and Work History, directed toward the pulmonary, cardiovascular, and gasrointestinal system.

2. D.O. Reviewed the employer's description of the individual's duties as they relate to asbestos exposure, the anticipated exposure level, the personal protective and respiratory equipment to be utilized by the individual, and any additonal medical information resulting from previous examination:

3. D.O. Conducted a physical examination of the individual with emphasis on the pulmonary, cardiovascular, and gastrointestinal systems, including a pulmonary function test of forced vital capacity (FVC) and forced expiratory volume at one second (FEV-1);

4. D.O. Determined that a chest roentgenogram ☒ was ☐ was not required as part of this examination.

5. D.O. Determined that this individual ☒ may ☐ may not use a respiratory device while performing his/her required employment services;

6. D.O. Informed this individual that I ☐ have ☒ have not detected a medical condition which would place this individual at an increased risk of material health impairment from exposure to asbestos;

7. D.O. Informed this individual of the results of my examination and of any medical condition that may result from this individual's exposure to asbestos;

8. D.O. Informed this individual of the health risks involved in smoking, of the synergistic relationship between cigarette smoking and asbestos exposure in producing lung cancer, and that cessation of smoking will reduce the risk of lung cancer.

Comments and/or Limitations (if any):

Douglas E. Okpara, MD
Physician's Printed Name

Douglas Okpara, M.D.
Physician's Signature

310-631-631-5655
Physician's Phone No.

19301 S. Santa Fe Ave., Ste 120 – Rancho Dominguez, CA 90221
Physician's Address

HARBOR ENVIRONMENTAL GROUP, INC.

FIT TEST RECORD

Employee Name: Alejandro Espinosa

Social Security: xxx-xx-2108

EPA / AHERA School Attended: Ecologics Training Institute

Medical Respirator Approved By: Douglas Industrial Medical Clinic

Respirator # 1: North | TC-21C-203 | L
Make | NIOSH Approval # | Size

(Circle Appropriate Response)
Respiratory Type: (Half Face) Full Face PAPR
Testing Method: Isoamyl Acetate Protocol (Irritant Fume Protocol)
Fit Rating: (1) 2 3

Respirator # 2: _____
Make | NIOSH Approval # | Size

(Circle Appropriate Response)
Respirator Type: Half Face Full Face PAPR
Testing Method: Isoamyl Acetate Protocol Irritant Fume Protocol
Fit Rating: 1 2 3

Test Administrator: Jose Xochitiotzi Tested By: Jose Xochitiotzi
Date Tested: 12/5/2023 Date Renewal Due: 12/5/2024

Fit Key Rating

1=Proper seal, very comfortable 2=Proper seal, comfortable 3=Proper seal, fairly comfortable

PO Box 9476 | BREA, CA 92821 | PHONE: (714) 349-1317 | FAX: (714) 257-9681
LICENSE #936557 DOSH #970

ECOLOGICS™
TRAINING INSTITUTE

Certificate of Attendance

CERTIFICATE NUMBER

57355

This is to Certify that

ELOY SEPULVEDA

Has Completed the Course of

AHERA ASBESTOS ABATEMENT WORKER 8 HR. REFRESHER COURSE (SPANISH) CA-014-12

UNDER TSCA 206, FOR PURPOSES OF COMPLIANCE WITH 29 CFR 1926.1101 AND TITLE 8 CCR 1529 AND TITLE 8 CCR 5208.

ARMANDO DUCOING
DIRECTOR

October 19, 2024	E101924SWR 101924	October 19, 2025
COMPLETION DATE	CLASS NUMBER / STARTING DATE	CERTIFICATE EXPIRES

Ecologics Training Institute

2487 E. Orangethorpe Ave. Fullerton, CA 92831 . Ph (714) 632-8100. Fax (714) 635 8111 . www.ecologicsonline.com

DOUGLAS INDUSTRIAL MEDICAL CLINIC

PHYSICIAN'S WRITTEN OPINION – ASBESTOS

COMPANY: HARBOR ENVIRONMENTAL

Applicant's Name: ELOY SEPULVEDA

Applicant's Address: 808 S. HOLLY AVE COMPTON, CA 90221

" The above named individual was seen by me on, 11/25/2023 and in accordance with all applicable portions of OSHA's Asbestos Standard for the Construction Industry, 29 CFR 1926.1101, with which I am familiar, I have indicated by initials, that I have performed the following."

1. D.O. Reviewed with this individual, his/her completed OSHA standardized Medical questionnaire and Work History, directed toward the pulmonary, cardiovascular, and gasrointestinal system.

2. D.O. Reviewed the employer's description of the individual's duties as they relate to asbestos exposure, the anticipated exposure level, the personal protective and respiratory equipment to be utilized by the individual, and any additonal medical information resulting from previous examination:

3. D.O. Conducted a physical examination of the individual with emphasis on the pulmonary, cardiovascular, and gastrointestinal systems, including a pulmonary function test of forced vital capacity (FVC) and forced expiratory volume at one second (FEV-1);

4. D.O. Determined that a chest roentgenogram ☒ was ☐ was not required as part of this examination.

5. D.O. Determined that this individual ☒ may ☐ may not use a respiratory device while performing his/her required employment services;

6. D.O. Informed this individual that I ☐ have ☒ have not detected a medical condition which would place this individual at an increased risk of material health impairment from exposure to asbestos;

7. D.O. Informed this individual of the results of my examination and of any medical condition that may result from this individual's exposure to asbestos;

8. D.O. Informed this individual of the health risks involved in smoking, of the synergistic relationship between cigarette smoking and asbestos exposure in producing lung cancer, and that cessation of smoking will reduce the risk of lung cancer.

Comments and/or Limitations (if any): Wear hearing protection in noisy environment.

Douglas E. Okpara, MD
Physician's Printed Name

Douglas Okpara, M.D.
Physician's Signature

310-631-631-5655
Physician's Phone No.

19301 S. Santa Fe Ave., Ste 120 – Rancho Dominguez, CA 90221
Physician's Address

HARBOR ENVIRONMENTAL GROUP, INC.

FIT TEST RECORD

Employee Name: Eloy Sepulveda

Social Security: xxx-xx-3991

EPA / AHERA School Attended: Ecologics Training Institute

Medical Respirator Approved By: Douglas Industrial Medical Clinic

Respirator # 1: North (Make) TC-21C-203 (NIOSH Approval #) L (Size)

(Circle Appropriate Response)

Respiratory Type: Half Face Full Face PAPR

Testing Method: Isoamyl Acetate Protocol Irritant Fume Protocol

Fit Rating: 1 2 3

Respirator # 2: _____ (Make) _____ (NIOSH Approval #) _____ (Size)

(Circle Appropriate Response)

Respirator Type: Half Face Full Face PAPR

Testing Method: Isoamyl Acetate Protocol Irritant Fume Protocol

Fit Rating: 1 2 3

Test Administrator: Jose Xochitiotzi Tested By: Jose Xochitiotzi

Date Tested: 11/25/2023 Date Renewal Due: 11/25/2024

Fit Key Rating

1=Proper seal, very comfortable 2=Proper seal, comfortable 3=Proper seal, fairly comfortable


PO Box 9476 I BREA, CA 92821 I PHONE: (714) 349-1317 I FAX: (714) 257-9681
LICENSE #936557 DOSH #970

10.0 SCHEMATIC

Copyright © 2024

All Rights Reserved

N

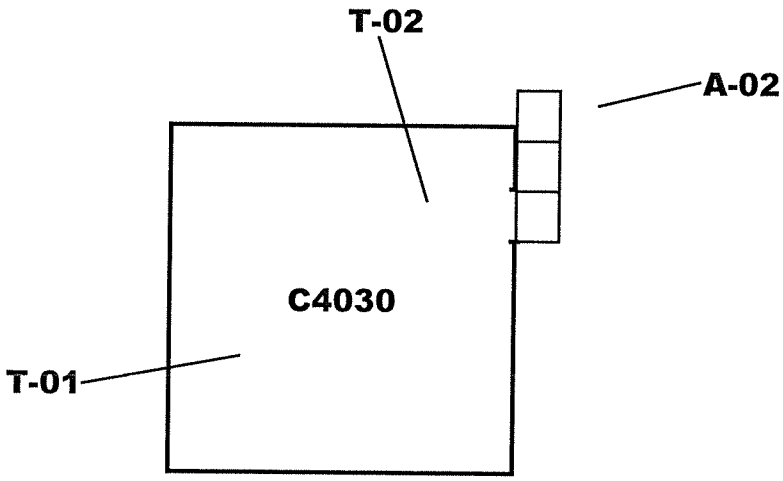

PROJECT NAME: CSULA - KING HALL - 4TH FLOOR - ROOM C4030

PROJECT NUMBER: E224-316
